Hutt River City Centre Upgrade Project: Preliminary Design

Draft Mon 16/05/16 4:06 p.m.

ID	Task Name
1	**1 Project approvals**
2	1.1 GW/HCC/NZTA approve preparing NOR/Consent
3	1.2 HVFMS recommends preparing NOR/Consents
4	1.3 GW/HCC/NZTA workshops
5	1.4 HVFMS endorses preliminary design and costs for further work
6	1.5 GW/HCC/NZTA workshops
7	1.6 Preliminary Design
8	1.7 HVFMS endorses the project s
9	**2 Cost Estimates/Funding City Centr**
10	2.1 Preliminary Cost Estimate
11	2.2 Final cost estimate
12	2.3 Funding/Implementation
13	**3 HVFMS Meetings**
14	3.1 Meeting March 2016
15	3.2 Meeting May 2016
16	3.3 Meeting June 2016
17	3.4 Meeting August 2016
18	3.5 Meeting September 2016
19	3.6 Local Authority Elections
20	3.7 Proposed March 2017
21	3.8 Proposed May 2017
22	3.9 Proposed September 2017
23	4 Iwi Liaison
24	**5 Community Engagement**
25	5.1 Communication Strategy
26	5.2 Newsletters
27	5.3 Responding to Stage 1 submitters
28	5.4 Landowners of land required, Meetings letter updates
29	5.5 Adjacent landowner letters
30	5.6 Stakeholder meetings
31	5.7 Update GW Web Page
32	**6 Procurement of consultancy servi**
36	**7 Preliminary Design and Costing**
82	**8 Stormwater**
85	**9 Planning and legal**
90	**10 Property Acquisition**
95	**11 Melling Intersection**
99	**12 Implementation/Financial**
105	**13 Preliminary Design Report**

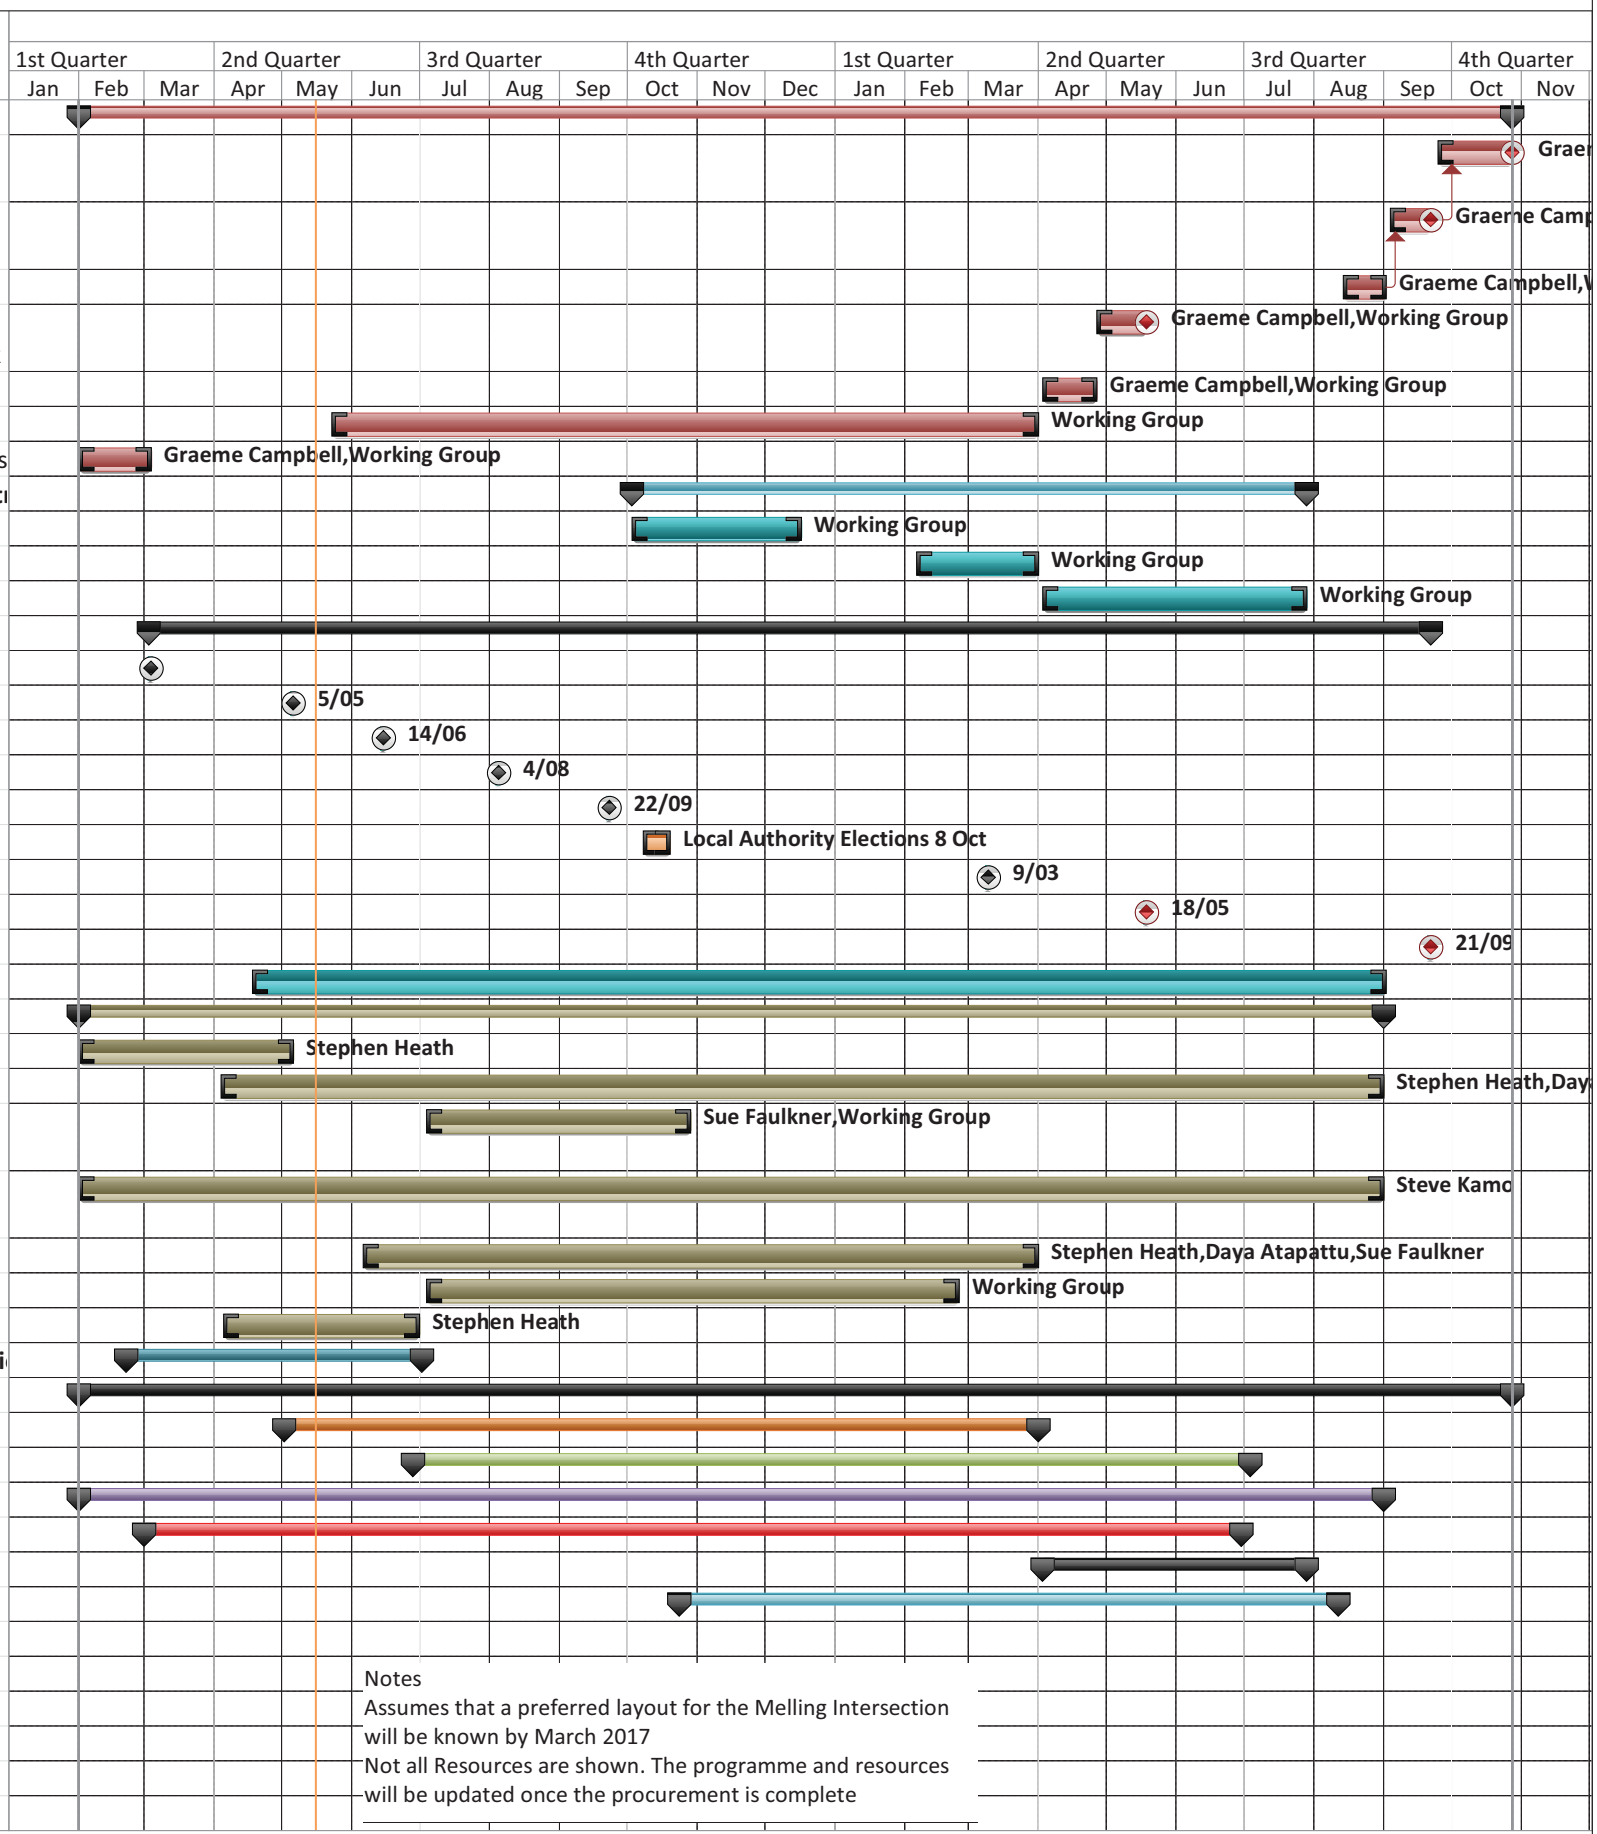

Notes
Assumes that a preferred layout for the Melling Intersection will be known by March 2017
Not all Resources are shown. The programme and resources will be updated once the procurement is complete
